North Fork Flathead Road Corridor Study - Updated Tue 6/1/10

ID	Task#	Task Name	Duration	Start	Finish	% Complete
1	0	Notice to Proceed	1 day	Mon 3/1/10	Mon 3/1/10	100%
2	1	Project Management	130 days	Tue 3/2/10	Mon 8/30/10	50%
3	2	Project Start-Up Meeting	37 days	Tue 3/2/10	Wed 4/21/10	100%
4	2	MDT to Provide a List of Invitees	19 days	Tue 3/2/10	Sat 3/27/10	100%
5	2	MDT to Provide Large Scale Regional Map for Start-Up Meeting	32 days	Tue 3/2/10	Wed 4/14/10	100%
6	2	MDT to Organize Tour and Provide Vehicle Transport	36 days	Tue 3/2/10	Tue 4/20/10	100%
7	2	Prepare for Start-Up/Resource Agency Meeting	14 days	Thu 4/1/10	Tue 4/20/10	100%
8	2	Conduct Start-Up/Resource Agency Meeting	1 day	Wed 4/21/10	Wed 4/21/10	100%
9	3	Baseline Mapping & Graphic Standards	127 days	Tue 3/2/10	Wed 8/25/10	50%
10	3.1	MDT to Provide Aerial Maps and GIS Layers	127 days	Tue 3/2/10	Wed 8/25/10	50%
11	3.1	MDT and PB to Develop Graphic Templates	127 days	Tue 3/2/10	Wed 8/25/10	50%
12	3.1	Review Corridor Mapping and GIS Data	124 days	Tue 3/2/10	Fri 8/20/10	50%
13	4	Corridor Needs & Objs, Existing Conditions & Roadway Ops	60 days?	Mon 3/22/10	Mon 6/14/10	86%
14	4.1	Develop Purpose, Needs and Objectives	35 days?	Tue 4/20/10	Mon 6/7/10	75%
15	4.1	MDT and FHWA Review of Purpose Needs and Objectives	5 days	Tue 6/8/10	Mon 6/14/10	0%
16	4.2	MDT to Provide the Latest Photo Log	0 days	Fri 5/7/10	Fri 5/7/10	100%
17	4.2	MDT to Provide As-Built Drawings	0 days	Mon 3/22/10	Mon 3/22/10	100%
18	4.2	MDT to Provide Historical Traffic and Crash Data	0 days	Mon 5/10/10	Mon 5/10/10	100%
19	4.2	Analyze the Photo Log and As-Built Drawings	10 days	Fri 5/7/10	Thu 5/20/10	100%
20	4.2	Analyze the Traffic and Crash Data (new data from MDT rece'd 5/10)	5 days	Mon 5/10/10	Fri 5/14/10	100%
21	4.3	MDT and Flathead County Will Provide Copies of Existing Geotechnical Reports	0 days	Fri 5/7/10	Fri 5/7/10	100%
22	4.3	MDT to Provide AASHTO and MDT Standards to be Used for the Corridor	2 days	Tue 3/23/10	Wed 3/24/10	100%
23	4.3	MDT Geotechnical Staff Site Visit and Summary to PB	0 days	Wed 4/28/10	Wed 4/28/10	100%
24	4.3	Roadway Users Information Gathering	40 days	Tue 3/23/10	Mon 5/17/10	100%
25	4.3	Review and Analyze Roadway Users Information	20 days	Thu 4/22/10	Wed 5/19/10	75%
26	4.3	Review and Analyze Roadway Deficiencies	16 days	Fri 5/7/10	Fri 5/28/10	100%
27	4.3	Review and Analyze Geotechnical Information	5 days	Fri 5/7/10	Thu 5/13/10	90%
28	4.4	MDT to Provide Parcel Map Information for Adjacent Parcels	10 days	Tue 3/23/10	Mon 4/5/10	100%
29	4.4	MDT will Coordinate with USFS, Flathead County to obtain ROW Information	10 days	Tue 3/23/10	Mon 4/5/10	100%
30	4.4	Review ROW Information Provided by MDT	40 days	Tue 3/23/10	Mon 5/17/10	80%
31	4.4	Prepare Mailing List from ROW Information	2 days	Tue 3/23/10	Wed 3/24/10	100%
32	5	Public Involvement (PI)	127 days	Tue 3/2/10	Wed 8/25/10	46%
33	5.1	MDT Will Provide an Initial List of Key Players	10 days	Tue 3/2/10	Mon 3/15/10	100%
34	5.1	MDT Will Provide Contact Information of Known Contacts	10 days	Tue 3/2/10	Mon 3/15/10	100%
35	5.1	MDT Will Make Resource Agency Contacts	15 days	Tue 3/2/10	Mon 3/22/10	100%
36	5.1	Develop Public Involvement Plan	40 days	Mon 3/15/10	Fri 5/7/10	100%
37	5.1	Submit Public Involvement Plan to MDT for Review	0 days	Fri 5/7/10	Fri 5/7/10	100%
38	5.1	MDT Review of Public Involvement Plan	2 days	Mon 5/10/10	Tue 5/11/10	100%
39	5.1	Revise Public Involvement Plan if Needed Based Upon MDT Comments	2 days	Wed 5/12/10	Thu 5/13/10	100%
40	5.2	Respond to and Track Public Comments	127 days	Tue 3/2/10	Wed 8/25/10	47%
41	5.3	Stakeholder Interviews: Preparation, Interviews and Summarize	40 days	Mon 4/12/10	Fri 6/4/10	40%
42	**5.3**	**Prepare Public Information Materials**	**53 days**	**Wed 5/12/10**	**Fri 7/23/10**	**10%**
43	5.3	PB prepare Newsletter #1	16 days	Wed 5/12/10	Wed 6/2/10	23%
44	5.3	MDT to review Newsletter #1	2 days	Thu 6/3/10	Fri 6/4/10	0%
45	5.3	PB to distribute Newsletter #1	1 day	Mon 6/7/10	Mon 6/7/10	0%
46	5.3	PB prepare Newsletter #2	15 days	Wed 6/30/10	Tue 7/20/10	0%
47	5.3	MDT to review Newsletter #2	2 days	Wed 7/21/10	Thu 7/22/10	0%
48	5.3	PB to distribute Newsletter #2	1 day	Fri 7/23/10	Fri 7/23/10	0%
49	5.3/4	MDT Review of Public Information Materials	125 days	Tue 3/2/10	Mon 8/23/10	24%
50	5.4	Schedule, Advertise and Prepare for PI Meeting #1	30 days	Tue 3/9/10	Mon 4/19/10	100%
51	5.4	Public Information Meeting #1	1 day	Tue 4/20/10	Tue 4/20/10	100%
52	5.4	Schedule, Advertise and Prepare for PI Meeting #2	40 days	Tue 6/1/10	Mon 7/26/10	5%
53	5.4	Public Information Meeting #2	1 day	Tue 7/27/10	Tue 7/27/10	0%
54	6	Future Transportation-Land Use, Demographics & Travel Needs	67 days	Mon 3/1/10	Wed 6/2/10	97%
55	6	MDT Will Provide Existing Traffic Volumes and Traffic Mix Data	0 days	Mon 3/1/10	Mon 3/1/10	100%
56	6	MDT Will Provide Relevant Planning Documents	0 days	Wed 3/10/10	Wed 3/10/10	100%
57	6	Review Existing Traffic Volumes and Traffic Mix Data	27 days	Wed 4/14/10	Thu 5/20/10	100%
58	6	Obtain Existing and Future Visitation Information for Glacier N.P.	8 days	Fri 5/14/10	Tue 5/25/10	100%
59	6	Obtain Available Data from Local Jurisdictions	24 days	Fri 4/23/10	Wed 5/26/10	100%
60	6	Develop Estimates of Future Traffic Volumes	2 days	Tue 6/1/10	Wed 6/2/10	0%
61	7	Environmental Studies	9 days	Mon 5/17/10	Thu 5/27/10	80%
62	7	MDT to Provide Environmental Resources Information	0 days	Mon 5/17/10	Mon 5/17/10	100%
63	7	Review Env. Data Provided by MDT, Draft Env. Conditions Section	9 days	Mon 5/17/10	Thu 5/27/10	80%
64	8	Improvement Options (IO)	9 days	Thu 6/3/10	Tue 6/15/10	0%
65	8	Identify & Discuss Improvement Options via teleconference	1 day	Thu 6/3/10	Thu 6/3/10	0%
66	8	Prepare meeting minutes	2 days	Fri 6/4/10	Mon 6/7/10	0%
67	8	Identify and Evaluate Improvement Options	5 days	Fri 6/4/10	Thu 6/10/10	0%
68	8	Prepare Conceptual Cost Estimates for Improvement Options	3 days	Fri 6/11/10	Tue 6/15/10	0%
69	8	MDT to Identify Potential Funding Sources and Provide to PB	0 days	Fri 6/11/10	Fri 6/11/10	0%
70	9.6	Prepare Improvement Options to include in Draft CS document	2 days	Fri 6/11/10	Mon 6/14/10	0%
71	9	Prepare Corridor Study (CS) Document	54 days	Tue 6/15/10	Fri 8/27/10	0%
72	9.1	Prepare Staff Review Draft CS Document and Submit to MDT	10 days	Tue 6/15/10	Mon 6/28/10	0%
73	9.1	Concurrent MDT and Agency Review of Draft Document	5 days	Tue 6/29/10	Mon 7/5/10	0%
74	9.1	Receipt of Integrated Comments from MDT	0 days	Mon 7/5/10	Mon 7/5/10	0%
75	9.2	Respond to MDT and Agency Comments	2 days	Tue 7/6/10	Wed 7/7/10	0%
76	9.2	Prepare Public Review Draft Document and Distribute	3 days	Thu 7/8/10	Mon 7/12/10	0%
77	9.2	Public Review Period	20 days	Tue 7/13/10	Mon 8/9/10	0%
78	9.3	Prepare Final Corridor Study Document	3 days	Tue 8/10/10	Thu 8/12/10	0%
79	9.3	MDT Review of Final Corridor Study	3 days	Fri 8/13/10	Tue 8/17/10	0%
80	9.3	Final Revisions to Corridor Study	3 days	Wed 8/18/10	Fri 8/20/10	0%
81	9.3	Prepare Distribution Copies of Final Study & Microstation Files	5 days	Mon 8/23/10	Fri 8/27/10	0%

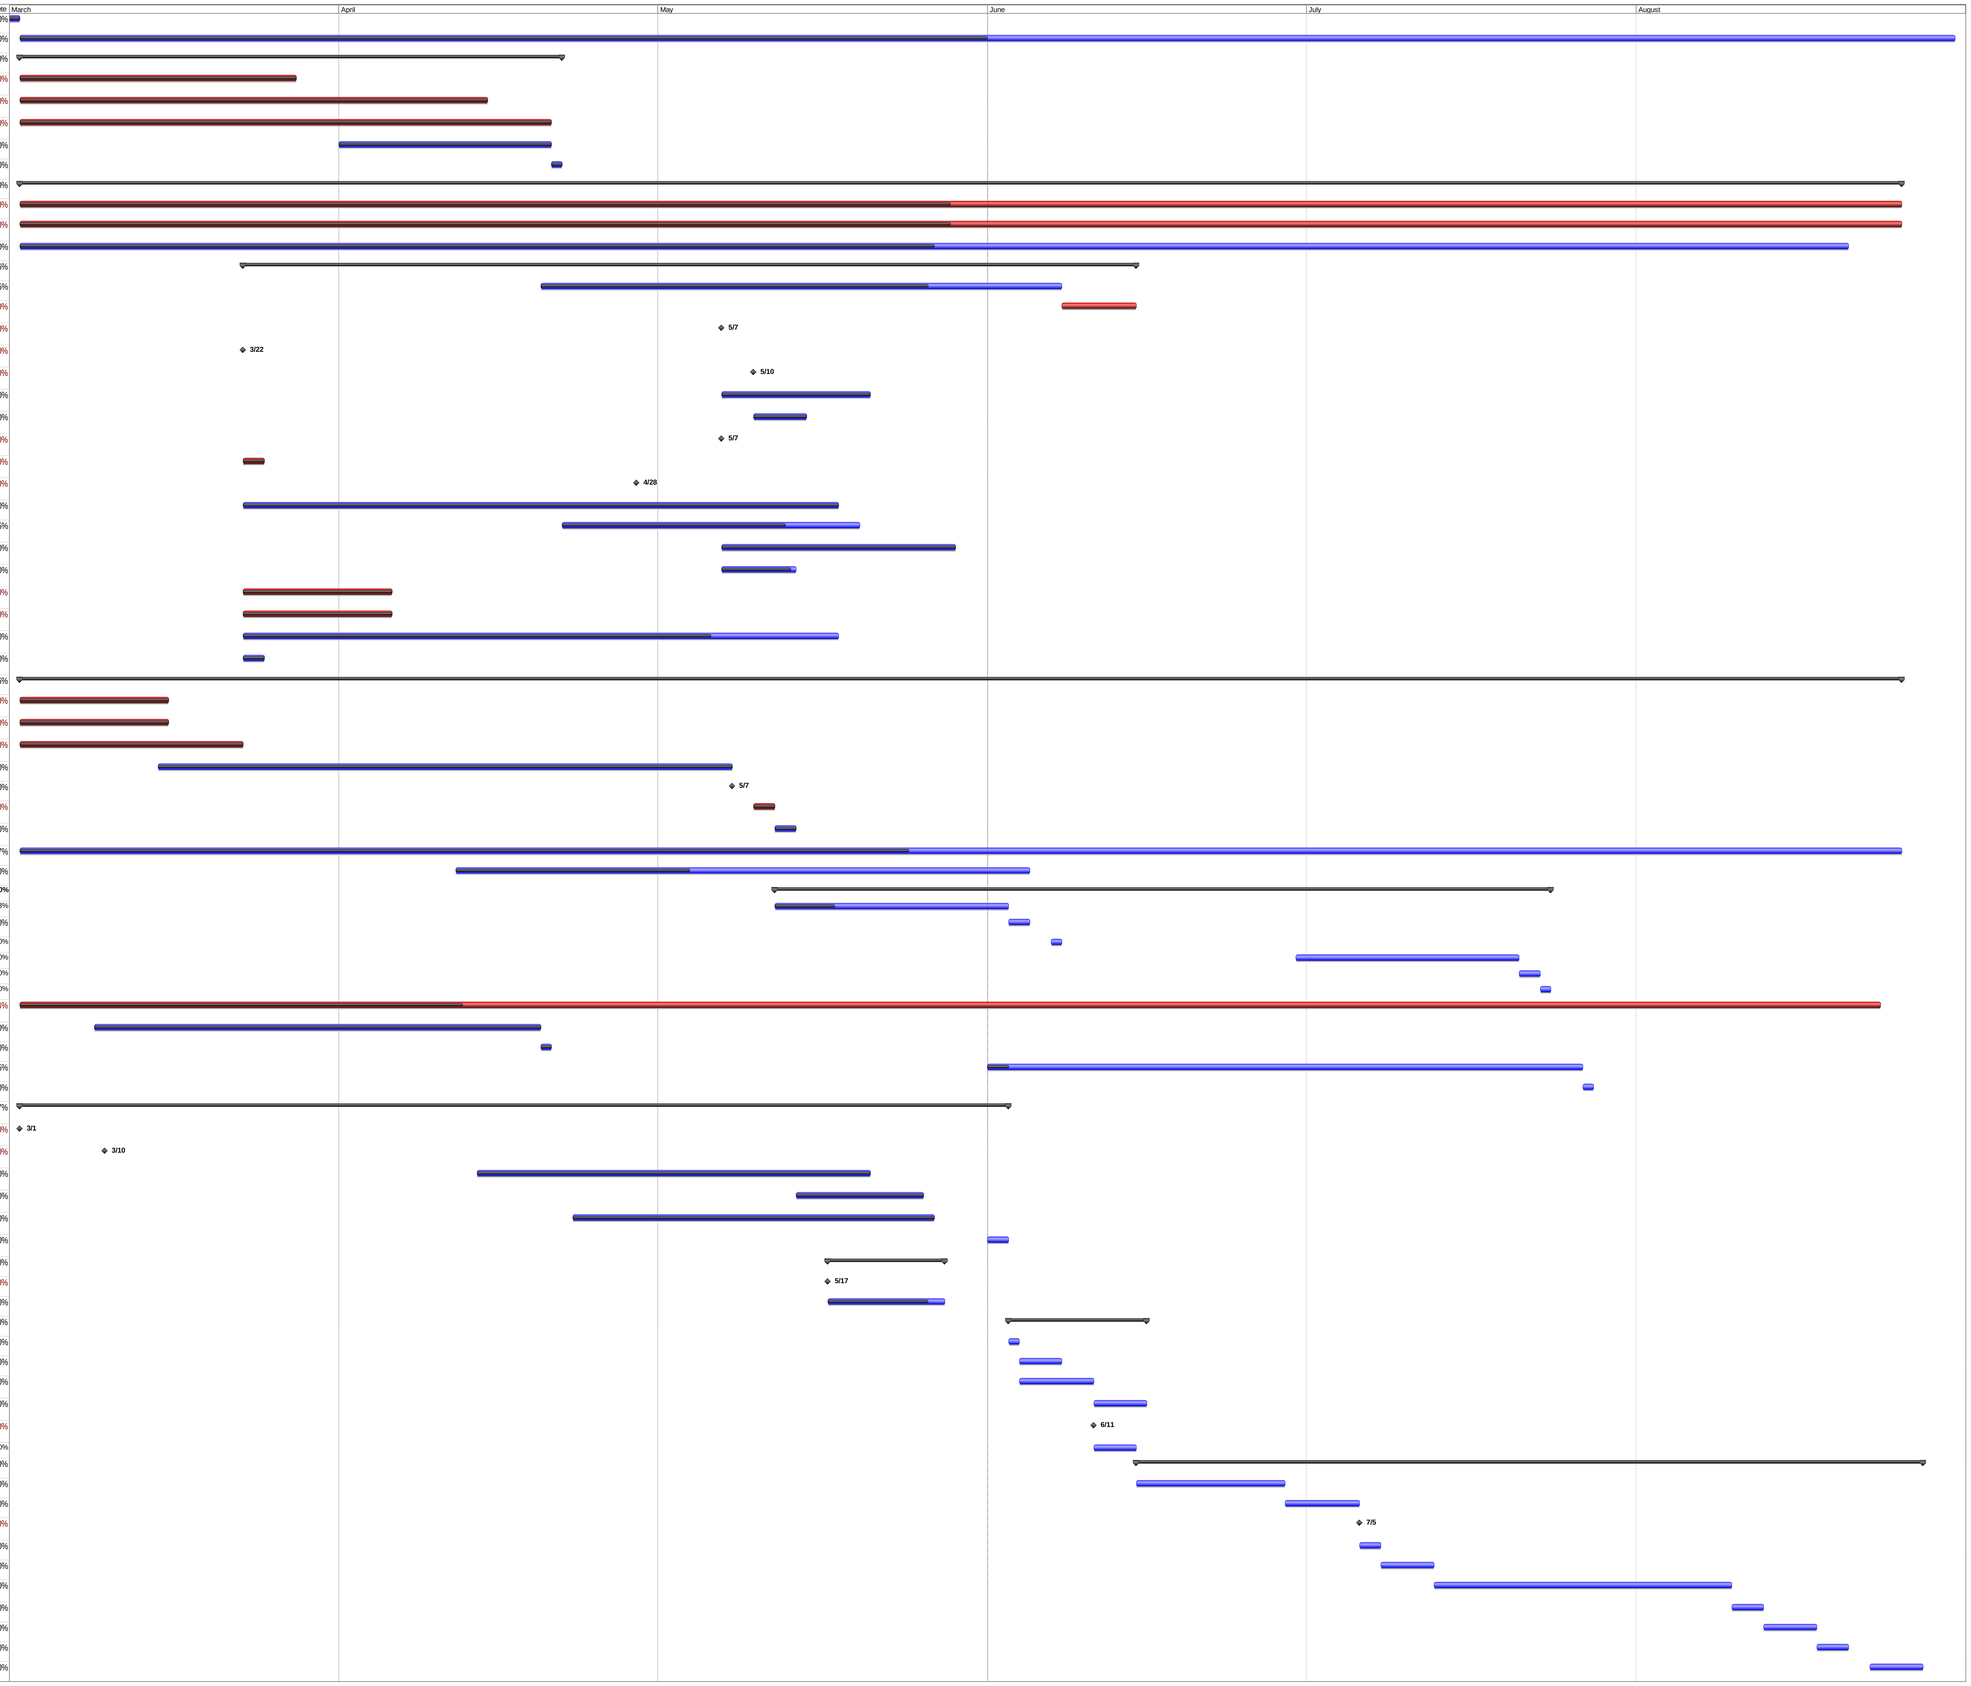

Project: NFFRCor
Date: Tue 6/1/10

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External Milestone | Deadline
